

Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Patient Health Record Consent Management System

Name: Harshit Vaish SRN: PES1UG24AM116 Section: B Date: 01 October 2026

1. Epics and User Stories (Backlog)

Our Lab 1 requirements were grouped into 5 Epics: Consent Granting & Access Requests (SCRUM-11), Consent Revocation & Expiry Notifications (SCRUM-12), Audit Trail & Transparency (SCRUM-13), Emergency Access Override (SCRUM-14) and Security & Authentication (SCRUM-15). These were broken into 14 User Stories worth 68 story points, ranked by priority.

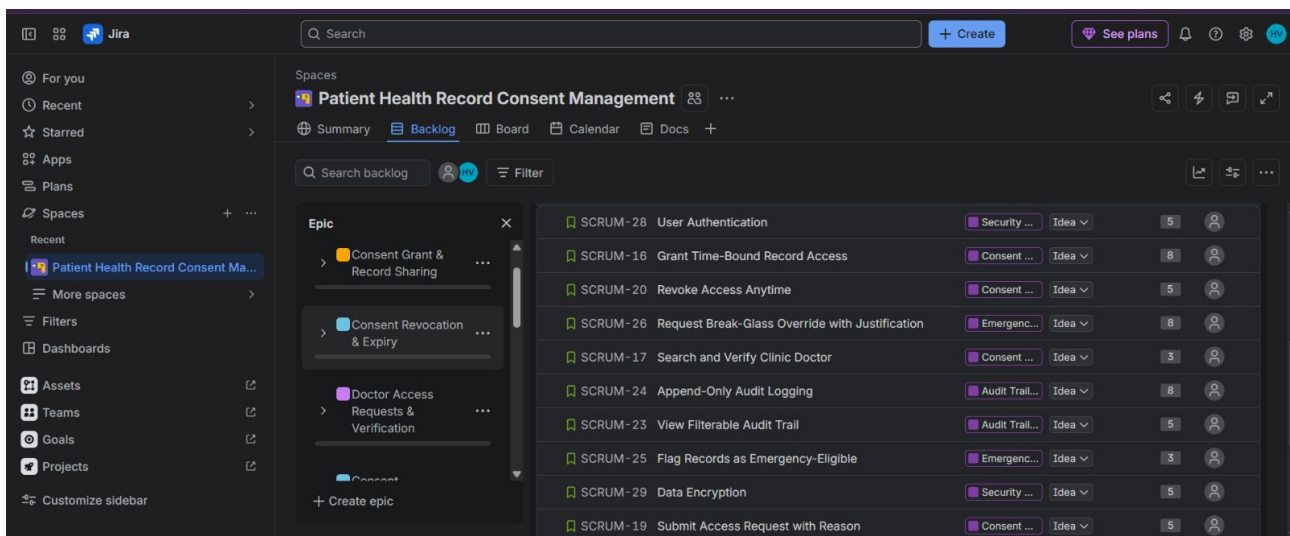


Figure 1: Backlog with the Epic panel open; each story shows its parent Epic and story points

2. Story Point Assignments and Sprint Planning

Story points were assigned using Fibonacci values (2, 3, 5, 8). Each sprint was planned at 34 points.

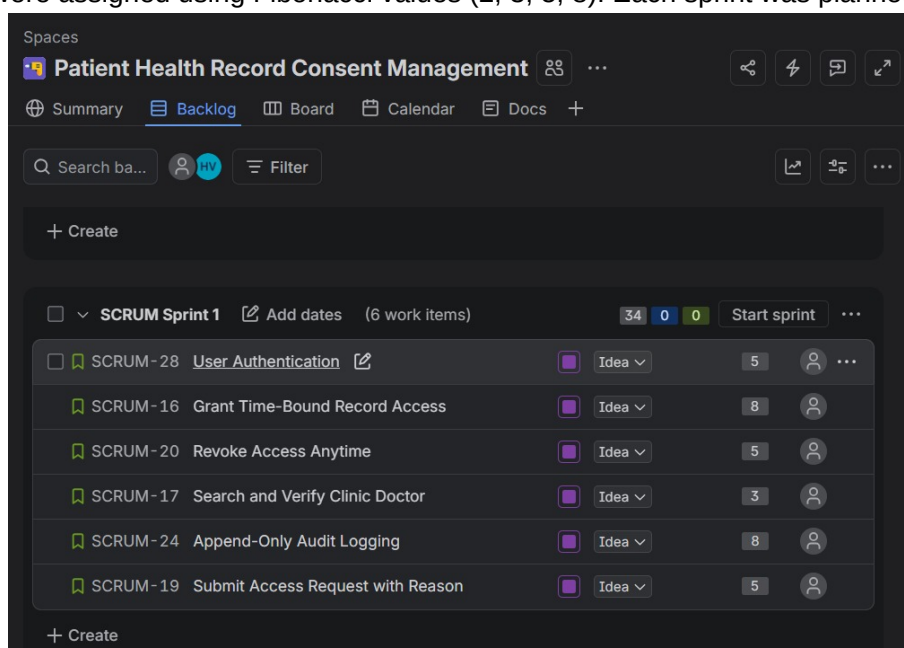


Figure 2: Sprint 1 - 6 stories, 34 story points

▼

SCRUM Sprint 2

Add dates

(8 work items)

34

0

0

Start sprint

...

SCRUM - 26

Request Break-Glass Override with Justification

Idea ▼

8

SCRUM - 23

View Filterable Audit Trail

Idea ▼

5

SCRUM - 25

Flag Records as Emergency-Eligible

Idea ▼

3

SCRUM - 29

Data Encryption

Idea ▼

5

SCRUM - 21

Expiry Reminder Notification

Idea ▼

5

SCRUM - 18

Set Custom Expiry Duration

Idea ▼

3

SCRUM - 27

Post-Emergency Patient Notification

Idea ▼

3

SCRUM - 22

Notify Doctor of Grant/Revoke

Idea ▼

2

Figure 3: Sprint 2 - 8 stories, 34 story points

3. Burndown Charts

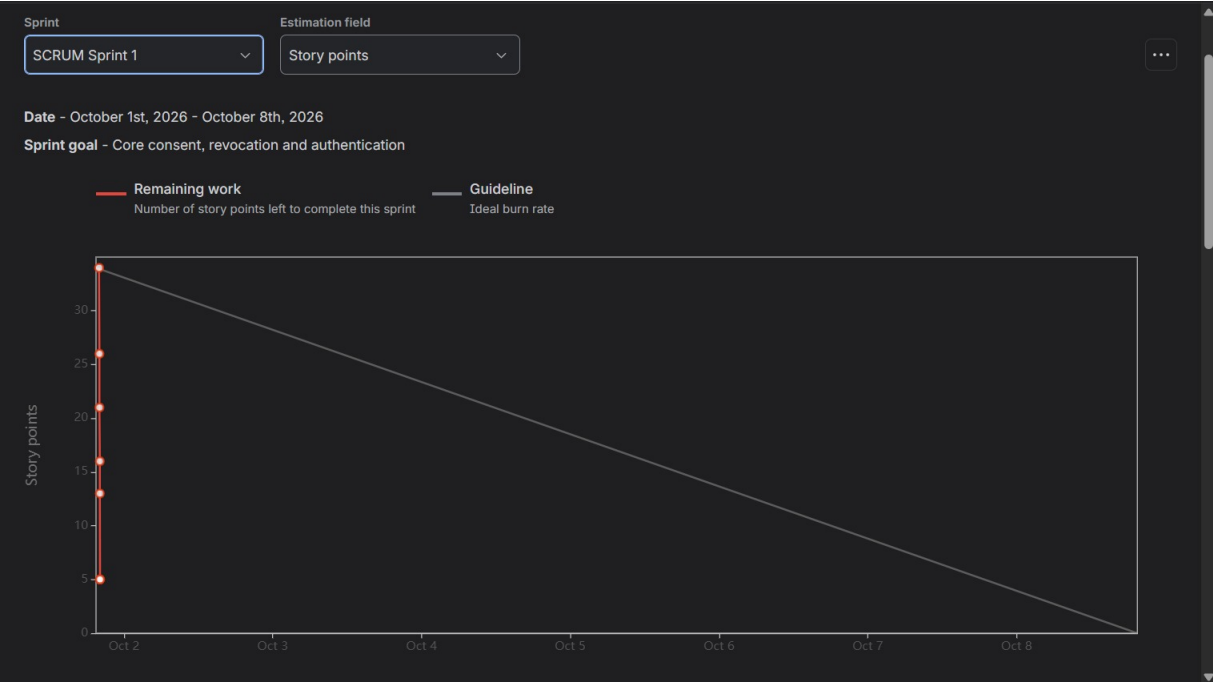


Figure 4: Sprint 1 burndown - 34 points committed, 29 completed, 5 carried over

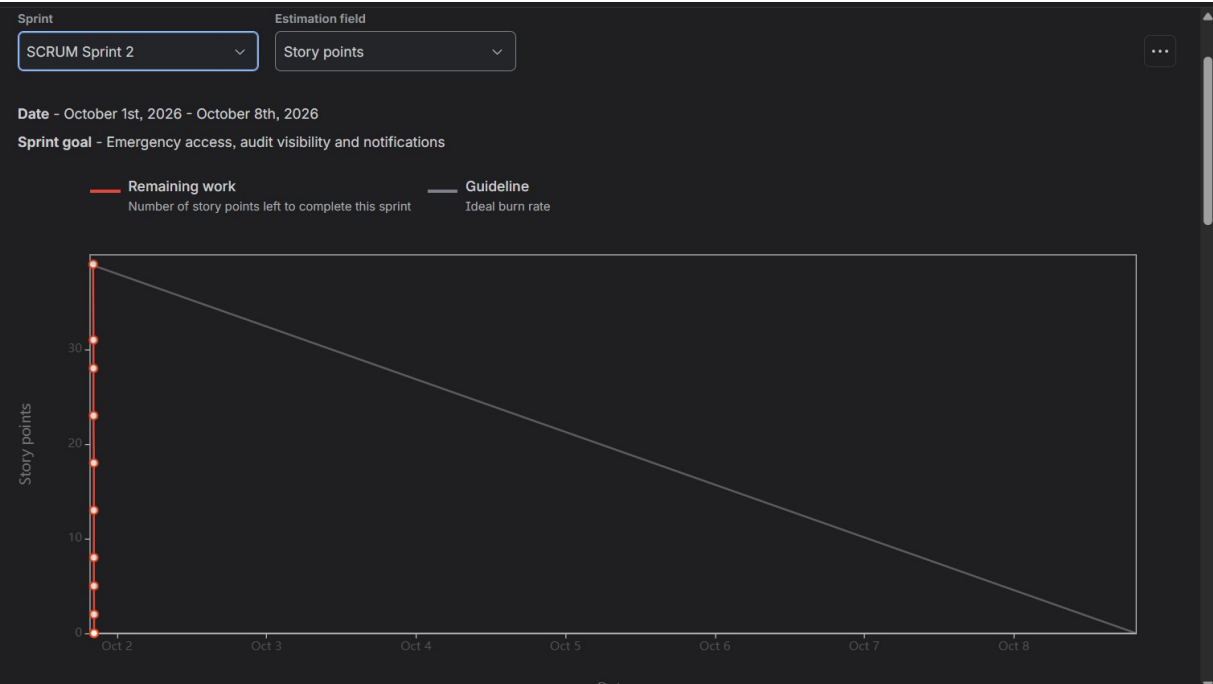


Figure 5: Sprint 2 burndown - 39 points committed (34 + 5 carried over), all completed

4. Sprint Board Outcome

Both sprints were run on the Active Sprint board, moving stories from To Do to In Progress to Done, and then completed. Because the sprints are now closed, the board outcome is shown through Jira's sprint summary of completed work items.

Completed work items							View in All work navigator
Key	Summary	Work type	Epic	Status	Assignee	Story points	
SCRUM-20	Revoke Access Anytime	Story	Consent Revo...	Done		5	
SCRUM-28	User Authentication	Story	Security & Au...	Done		5	
SCRUM-16	Grant Time-Bound Record Access	Story	Consent Gran...	Done		8	
SCRUM-24	Append-Only Audit Logging	Story	Audit Trail & T...	Done		8	
SCRUM-17	Search and Verify Clinic Doctor	Story	Consent Gran...	Done		3	
Work items completed outside of sprint							

Figure 6: Sprint 1 completed work items - 5 stories, 29 points (SCRUM-19 carried over)

Completed work items							View in All work navigator
Key	Summary	Work type	Epic	Status	Assignee	Story points	
SCRUM-26	Request Break-Glass Override with Justification	Story	Emergency A...	Done		8	
SCRUM-21	Expiry Reminder Notification	Story	Consent Revo...	Done		5	
SCRUM-23	View Filterable Audit Trail	Story	Audit Trail & T...	Done		5	
SCRUM-25	Flag Records as Emergency-Eligible	Story	Emergency A...	Done		3	
SCRUM-18	Set Custom Expiry Duration	Story	Consent Gran...	Done		3	
SCRUM-29	Data Encryption	Story	Security & Au...	Done		5	
SCRUM-22	Notify Doctor of Grant/Revoke	Story	Consent Revo...	Done		2	
SCRUM-27	Post-Emergency Patient Notification	Story	Emergency A...	Done		3	
SCRUM-19	Submit Access Request with Reason	Story	Consent Gran...	Done		5	

Figure 7: Sprint 2 completed work items - 9 stories, 39 points (including carried-over SCRUM-19)

5. Reflection

Our Jira SCRUM project broke the system into 5 epics and 14 user stories worth 68 story points, estimated with Fibonacci values (2, 3, 5, 8) in a Planning Poker style discussion. We ran two one-week sprints and delivered all 68 points.

5.1 Did our estimations reflect the actual effort?

Mostly yes. Sprint 2 finished all 39 committed points, and Sprint 1 finished 29 of 34, so our estimates were broadly usable. The one miss was SCRUM-19 "Submit Access Request with Reason" (5 points), which we did not finish in Sprint 1. We think the 8-point stories (Grant Time-Bound Access, Append-Only Audit Logging and Emergency Override) carried the most risk, because they combined the most unknowns and the most dependencies. All three were delivered, but their estimates had the widest margin for error, and we would split them next time. Because this was a simulation, we cannot say how closely the points would match real hours.

5.2 Was our backlog well-prioritised?

We think so. We ranked the Highest-priority stories first (User Authentication, Grant Time-Bound Access, Revoke Access and Emergency Override), so the core consent flow and security foundations were in place early. Lower-risk notification and reminder stories were left for the end, and slipping any of those would have cost little. One weakness is that SCRUM-19 sits naturally beside the access-grant work, so leaving it at the edge of Sprint 1 made it the obvious story to spill over.

5.3 How did our simulated sprint align with our plan?

Sprint 1 (goal: "Core consent, revocation and authentication") committed 34 points across 6 stories and completed 29. Sprint 2 (goal: "Emergency access, audit visibility and notifications") committed 39 points, which was the 34 planned plus the 5 carried over, and completed all 39. Sprint 2's goal was fully met; Sprint 1's goal was only completed after SCRUM-19 was finished in Sprint 2. The Sprint 1 carry-over suggests we over-committed slightly. Sprint 2 then carried a heavier load than planned and still finished, which tells us our capacity may be higher than Sprint 1 showed.

5.4 What insights did the burndown chart give about our team's capacity?

In the Sprint 1 burndown, the remaining-work line stepped down from 34 and stopped at 5 instead of reaching zero, showing the unfinished story. The Sprint 2 line started higher than planned at 39 because of the carry-over, and reached zero. In both charts the red line dropped almost vertically on the first day and stayed well below the grey guideline, because we moved all the cards within minutes rather than across the week.

Our velocity was 29 points in Sprint 1 and 39 in Sprint 2, an average of 34 points per sprint. Planning around 30 to 34 points per sprint would be a safer commitment than the 34 to 39 we used. An important caveat: this was a simulation, so the burndown reflects simulated rather than real work timing. The chart shows our planning and completion totals but not real pacing or day-to-day capacity. We would only trust it as a capacity signal after a sprint with real effort and real dates.

Takeaways

We would commit slightly fewer points, split the 8-point stories, and put dependent stories in the same sprint. We would also re-estimate after a real sprint with real timing.
